9506B LEE HWY,

FAIRFAX, VA 22031 Phone: (571) 249-3448 www.plan-source.com

No.	DATE:	REVISIONS ▼
PROJ	ECT INF	ORMATION:

26065 POINT LOOKOUT RD LEONARDTOWN, MD 20650

OWNER'S NAME:

DASH IN FOOD STORES INC A MARYLAND CORPORATION

DEVELOPER INFORMATION:

THE WILLS GROUP, INC 102 CENTENNIAL ST, LA PLATA, MD 20646

DRAWING TITLE:

ΔRFΔ

E & SC-PHASE-II

ANLA.	42,674 SF(0.979 AC)		
SCALE:	AS SHOWN		
PROJECT MANAGER:			
KES			

DOCUMENT WITHOUT WRITTEN
CONSENT OF THE PLAN SOURCE,
INC. IS PROHIBITED.

KES				
DRAWN BY: GSD	DATE: NOV 2023			
CHECKED BY:	TAX ACCOUNT#:			
	017012			
THIS DESIGN IS COPYRIGHTED AND DRAWING NO. PROTECTED UNDER THE LAWS OF THE UNITED STATES OF AMERICA.	DRAWING NO. SITE DEVELOPMENT PLAN			

7 OF 36

PHASE II CONSTRUCTION SEQUENCE

TEMPORARY SEEDING

CONSTRUCTION ENTRANCE

- 1. CONTRACTOR TO VERIFY AND INSPECT THE EXISTING EROSION & SEDIMENT CONTROL
- 1. CONTRACTOR TO VERIFY AND INSPECT THE EXISTING EROSION & SEDIMENT CONTROL MEASURE AND REPAIRADD IF NECESSARY (1 DAY)
 2. BEGIN DEMOLITION OF EXISTING CARWASH, CONVENIENCE STORE, FUEL CANOPY AND UNDERGROUND STORAGE TANKS LAND DISTURBANCE ACTIVITIES. MAINTAIN POSITIVE DRAINAGE TO THE EXISTING INLETS AT ALL TIMES, (15 DAYS)
 3. START INSTALLATION OF STORM SEWER, SANITARY SEWER AND OTHER UTILITIES, PROVIDE INLET PROTECTION TO THE TRENCH INLET AND CURB INLETS. CONTINUE SITE GRADING TO PROPOSED FINISHED GRADES MAINTAINING POSITIVE DRAINAGE TO INLETS. INLET PROTECTION CANNOT BE REMOVED UNTIL AUTHORIZED BY THE TOWN ENVIRONMENTAL INSPECTOR (30 DAYS) INSPECTOR, (30 DAYS)

- INSPECTOR. (30 DAYS)

 4. INSTALL PROPOSED UNDERGROUND TANKS, AND ASSOCIATE HARDWARE. (10 DAYS)

 5. INSTALL PROPOSED UNDERGROUND DETENTION SYSTEM. (15 DAYS)

 6. START CONSTRUCTION OF INTERNAL PARKING, CURB AND GUTTER, AND DRIVE AISLES. INSTALL STONE BASE TO ALL PARKING AREAS TO SERVE AS TEMPORARY STABILIZATION AND INSTALL TEMPORARY SEEDING IN NEWLY GRADED AREAS, (90 DAYS)

 7. CONSTRUCT PROPOSED CONVENIENCE STORE AND FUEL CANOPY.

 8. PAVE PARKING AREAS, INSTALL PAVEMENT STRIPING, AND FULLY STABILIZE ON SITE IMPROVEMENTS. SWM FACILITIES CANNOT BE INSTALLED UNTIL 95% STABILIZATION OF THE CONTRIBUTING DRANAGE AREA. THE DEVELOPER SHALL NOTIFY THE TOWN AT LEAST FORTY. EIGHT (49) HOUR BEFORE COMMENCING ANY WORK IN CONJUNCTION WITH THE STORM WATER MANAGEMENT PLAN. (3 DAYS)
- FORTY- EIGHT (48) HOUR BEFORE COMMENCING ANY WORK IN CONJUNCTION WITH THE STORM WATER MANAGEMENT PLAN. (3 DAYS)

 9. REMOVE EROSION CONTROLS UPON FULL STABILIZATION OF ALL SITE IMPROVEMENTS AND COUNTY APPROVAL. NO EROSION AND SEDIMENT CONTROL MEASURES CAN BE REMOVED WITHOUT PERMISSION FROM THE TOWN / COUNTY ENVIRONMENTAL INSPECTOR. (2 DAYS)


 10. INSTALL FINAL LANDSCAPING AND PLANTINGS. STABILIZED DISTURBED AREAS ASSOCIATED WITH LANDSCAPING AND PLANTING THE SAME DAY. (7 DAYS)


 11. SITE CLEANUP/DEMOBILIZATION.(2 DAYS)

PHASE II MATERIAL SCHEDULE				
MATERIAL	QUANTITY	REMARKS		
SILT FENCE	500 LF	UTILIZED PHASE-I		
SILT FENCE ON PAVEMENT	400 LF	UTILIZED PHASE-I		
CONSTRUCTION FENCE	782 LF	UTILIZED PHASE-I		
INLET PROTECTION	4 EA			
STOCKPILE	1 EA			
LIMITS OF DISTURBANCE	0.86 AC			

0.03 AC

1 EA.



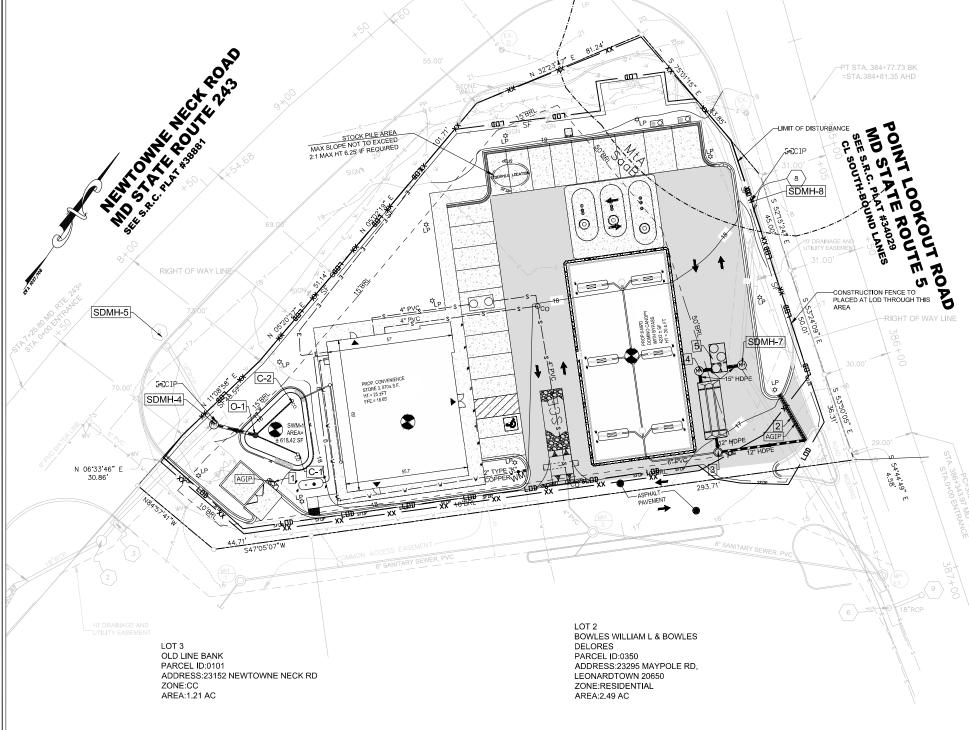

CUT REMOVAL NOTES:

1. ALL EXCAVATED TRENCH MATERIAL SHALL BE REMOVED WITH THE PERMISSION PERMISSION FROM THE TOWN / COUNTY ENVIRONMENTAL INSPECTOR.

IMMEDIATE STABILIZATION NOTES:

1. IMMEDIATE ACTION SHOULD BE TAKEN IN THE LOD BUMP OUTS FOR STABILIZATION AT TOP RIGHT-HAND SIDE AND LOWER RIGHT-HAND CORNER.

NOTES:
- THE CONTRACTOR MAY INSTALL MULCH/FILTER LOGS IN LIEU OF SFOP DEPENDING ON SITE
